

Annex C – Movement and Place Plans Programme

| MAP Plan | Development of MAP Plans | Internal OCC Engagement | District Officer Engagement | Councillor Engagement | Stakeholder Engagement | Public Engagement | Adoption |
|---------------------------------------|--------------------------|-------------------------|-----------------------------|-----------------------|------------------------|-------------------|-------------|
| Overview Chapter | Completed | Completed | N/A | N/A | N/A | November 25 | January 26 |
| Science Vale | Completed | Completed | Ongoing | Ongoing | Ongoing | November 25 | January 26 |
| Bicester & Mid Cherwell | Completed | Completed | Ongoing | Ongoing | Ongoing | November 25 | January 26 |
| West Oxfordshire Lowlands | Completed | Completed | December 25 - January 26 | February 26 | March 26 | April 26 | June 26 |
| Kidlington and South Cherwell | Completed | Completed | December 25 - January 26 | February 26 | March 26 | April 26 | June 26 |
| Abingdon and the East Vale | Ongoing | December - January 26 | February 26 | March 26 | March 26 | April 26 | June 26 |
| Banbury and North Cherwell | Ongoing | March-April 26 | April 26 | May 26 | June 26 | September 26 | November 26 |
| Wallingford and River Thames Corridor | January - March 26 | April - May 26 | June 26 | July 26 | July 26 | September 26 | November 26 |
| West Oxfordshire Uplands | January - March 26 | April - May 26 | June 26 | July 26 | July 26 | September 26 | November 26 |
| Thame, Chinor and Watlington | June - October 26 | November 26 | December 26 | December 26 | January 26 | February 27 | April 27 |
| Western Vale | June - October 26 | November 26 | December 26 | December 26 | January 26 | February 27 | April 27 |
| Henley-on-Thames | June - October 26 | November 26 | December 26 | December 26 | January 26 | February 27 | April 27 |

| | | | | | | | |
|----------------------------|-------------------------|-------------|-------------|-------------|------------|-------------|--------------|
| Oxfordshire Metro* | June - October 26 | November 26 | December 26 | December 26 | January 26 | February 27 | April 27 |
| Central Oxfordshire | December 26-February 27 | February 27 | March 27 | April 27 | May 27 | June 27 | October 2027 |

**Subject to
securing additional
funding*

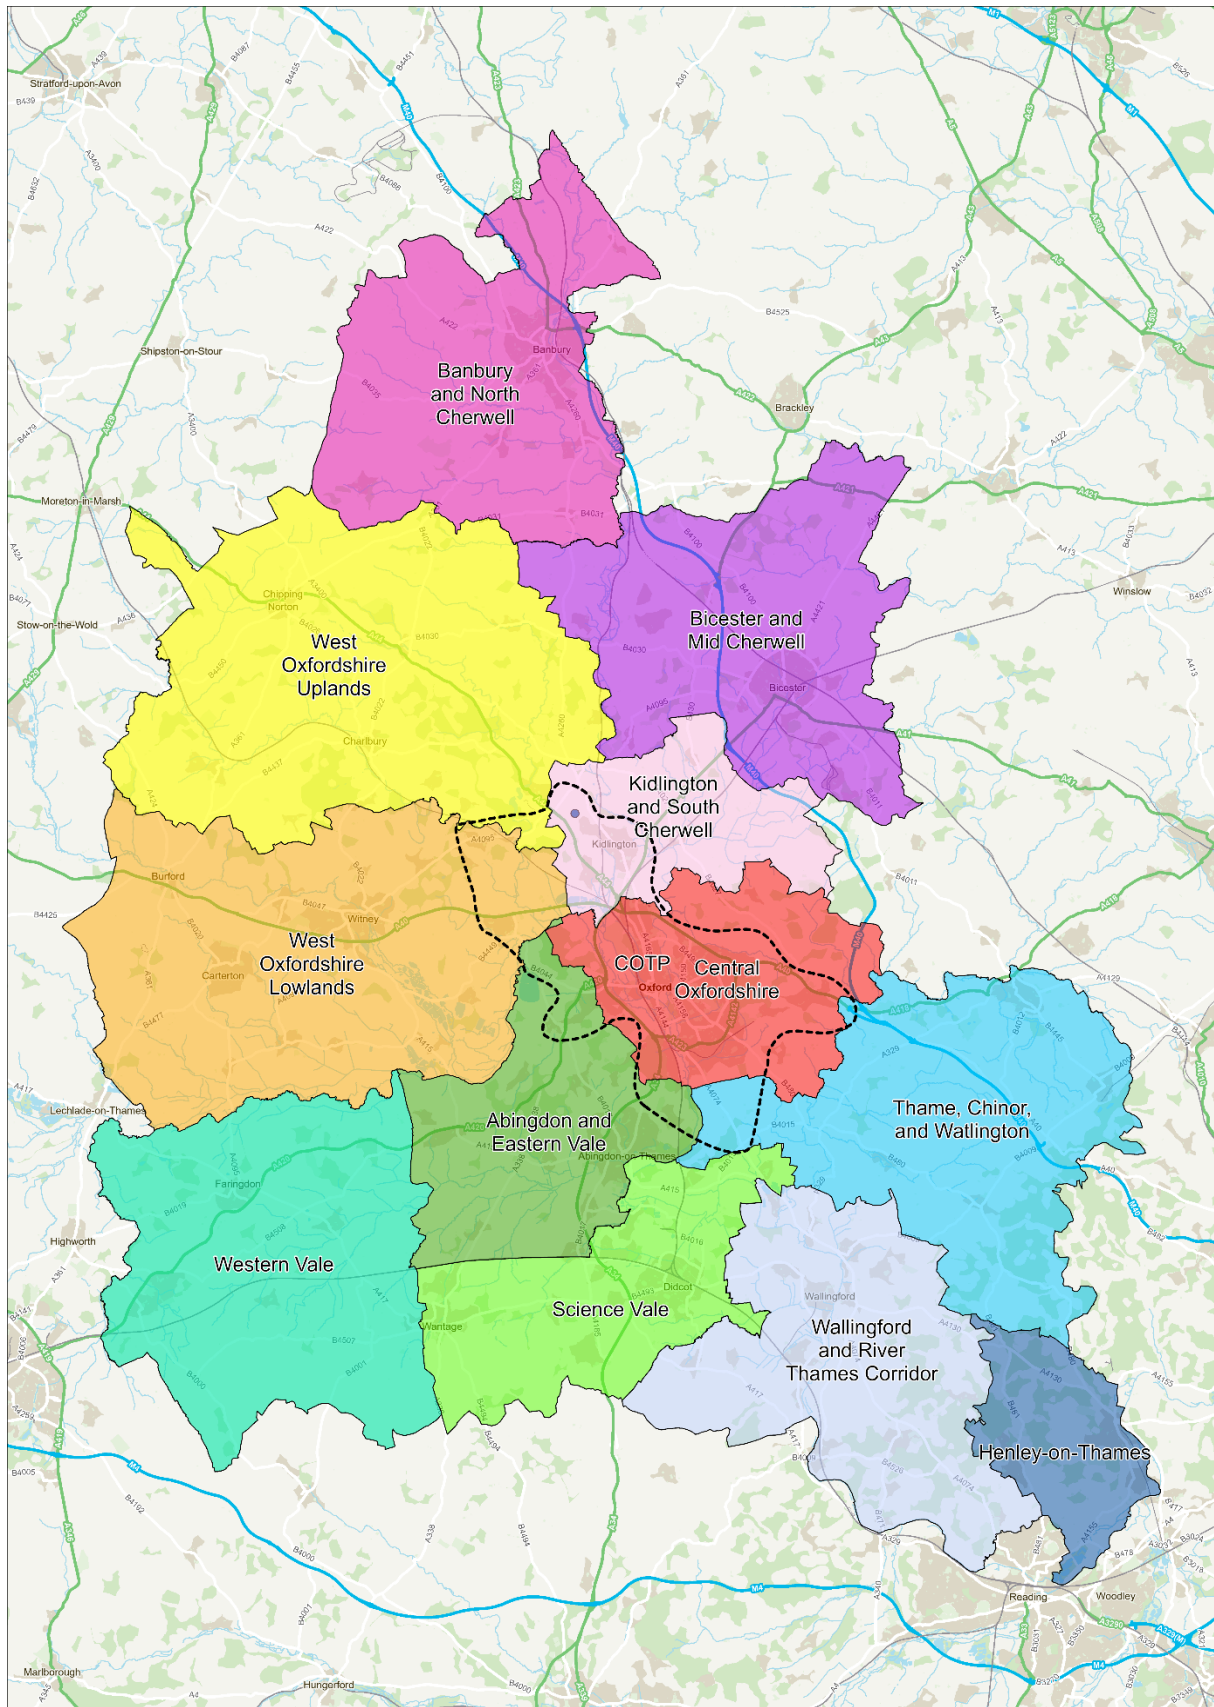


Figure 1, Proposed geographical boundaries of the Movement and Place Plans
